| Activity ID | Activity Description | Early Start | Early Finish |
|---|---|---|---|
| **Bill Shotton** | | | |
| 360 | Tribble Lobby Upgrade | 15JUN09 | 14AUG09 |
| 370 | Stadium - Phase IV | 02MAR09A | 10JUL09 |
| 380 | Faculty Apartments | 26MAY09 | 07AUG09 |
| 390 | Detamble Renovation | 29MAY09 | 31JUL09 |
| 400 | Carswell Renovations | 01JUN09 | 07AUG09 |
| 410 | Mag / Heratige / Autumn Room Renovations | 12JUN09 | 14AUG09 |
| 420 | Green Hall Rm 327 | 15JUN09 | 24JUL09 |
| 440 | UCC - Landscape Renovation | 01APR09 | 07AUG09 |
| **Ed Bullington** | | | |
| 120 | CHP UST Removal | 13APR09A | 31AUG09 |
| 130 | H2 Buildings | 12AUG08A | 31AUG09 |
| 140 | Water Tower | 15APR09A | 31JUL09 |
| 150 | Martin Hall Renovation | 15JUN09 | 03AUG09 |
| 160 | Anthropology Japan Gallery | 25MAY09 | 30JUN09 |
| 170 | Art Dept Sinks & Cabinets | 19MAY09A | 20AUG09 |
| 180 | Mainstage Theater Upfit | 19MAY09A | 20AUG09 |
| 190 | New Outdoor Activity Area | 06APR09A | 14AUG09 |
| 200 | Modernize/Replace Orchestra Pit Elevator | 01JUN09 | 17AUG09 |
| 210 | Winston Hall HVAC Upgrade Design | 01JUN09 | 31DEC09 |
| 220 | Upgrade Salem Hall Exhaust System | 01JUN09 | 29JAN10 |
| 230 | Fume Hood for Salem 14 | 01DEC09 | 29JAN10 |
| 240 | Scales Elevator Sump | 01JUN09 | 17AUG09 |
| 250 | Lighting Upgrade | 05JUN09 | 07JUN10 |
| 330 | Dance Studio | 15JUN09 | 30OCT09 |
| **Greg Scott** | | | |
| 10 | Scales Art Lobby Phase 1 | 26MAY09 | 07JUL09 |
| 20 | Scales Art Lobby Phase 2 | 01JUL09 | 07AUG09 |
| 30 | Winston Hall 121 Lab Renovation | 19MAY09A | 01JUL09 |
| 40 | Winston Hall 121 Cabinet Delivery & Install | 07JUL09 | 03AUG09 |
| 50 | Deans Office 104 | 21MAY09A | 01JUL09 |
| 60 | Student Apt B | 19MAY09A | 24JUL09 |
| 70 | Campus Mech Room Drainage | 02MAR09A | 15JUN09 |
| 80 | Reynolda Village 117B Elevator | 01MAY09A | 22JUN09 |
| RG100 | Reynolds Gym ACM Removal | 10DEC09 | 11JAN10 |
| RG90 | Reynolds Gym ACM Removal Design | 01SEP09 | 01DEC09 |
| **Keith Callahan** | | | |
| AB260 | New Admission Building Design | 18AUG08A | 30JUN09 |
| AB270 | New Admission Building Construction | 21AUG09 | 29OCT10 |
| AC300 | New Academic Building Design | 03NOV08A | 01APR10 |
| BC320 | Business Education Center Renovations Design | 11MAY09A | 31DEC09 |
| BC330 | Business Education Center Construction (IS) | 01JAN10 | 30JUL10 |
| BC340 | Business Education Center Construction (Worrell) | 02AUG10 | 31DEC10 |
| IS360 | IS Relocation to UCC Design | 21MAY09 | 30JUN09 |
| RC310 | New Recreation Center Design | 18AUG08A | 01APR10 |
| SW350 | New Storage Warehouse Concept Design | 21MAY09 | 30SEP09 |
| **Maintenance & Utilities** | | | |
| 260 | Replace 25 Ton DX Unit at Gym | 01MAY09A | 01FEB10 |
| 270 | Replace Obsolete Call Boxes(6) | 01JUN09 | 31AUG09 |
| 280 | South Chiller Design | 01JUN09 | 31DEC09 |
| 290 | Campus Water Meters / Backflows | 01APR09A | 31JUL09 |
| 300 | Sanitary Sewer Ph 2 & 3 | 01APR09A | 31JUL09 |
| 310 | Condensate Replacement in Tunnels Ph 5 | 02FEB09A | 31JUL09 |
| 320 | Campus Elevator Upgrades - 8 ADA Phones | 01JUN09 | 31JUL09 |
| **Ryan Swanson** | | | |
| BF110 | Benson Food Court Renovations | 01OCT08A | 17AUG09 |
| RH280 | New Residence Hall Design | 18AUG08A | 29MAY09 |
| RH290 | New Residence Hall Construction | 01JUN09 | 30JUL10 |

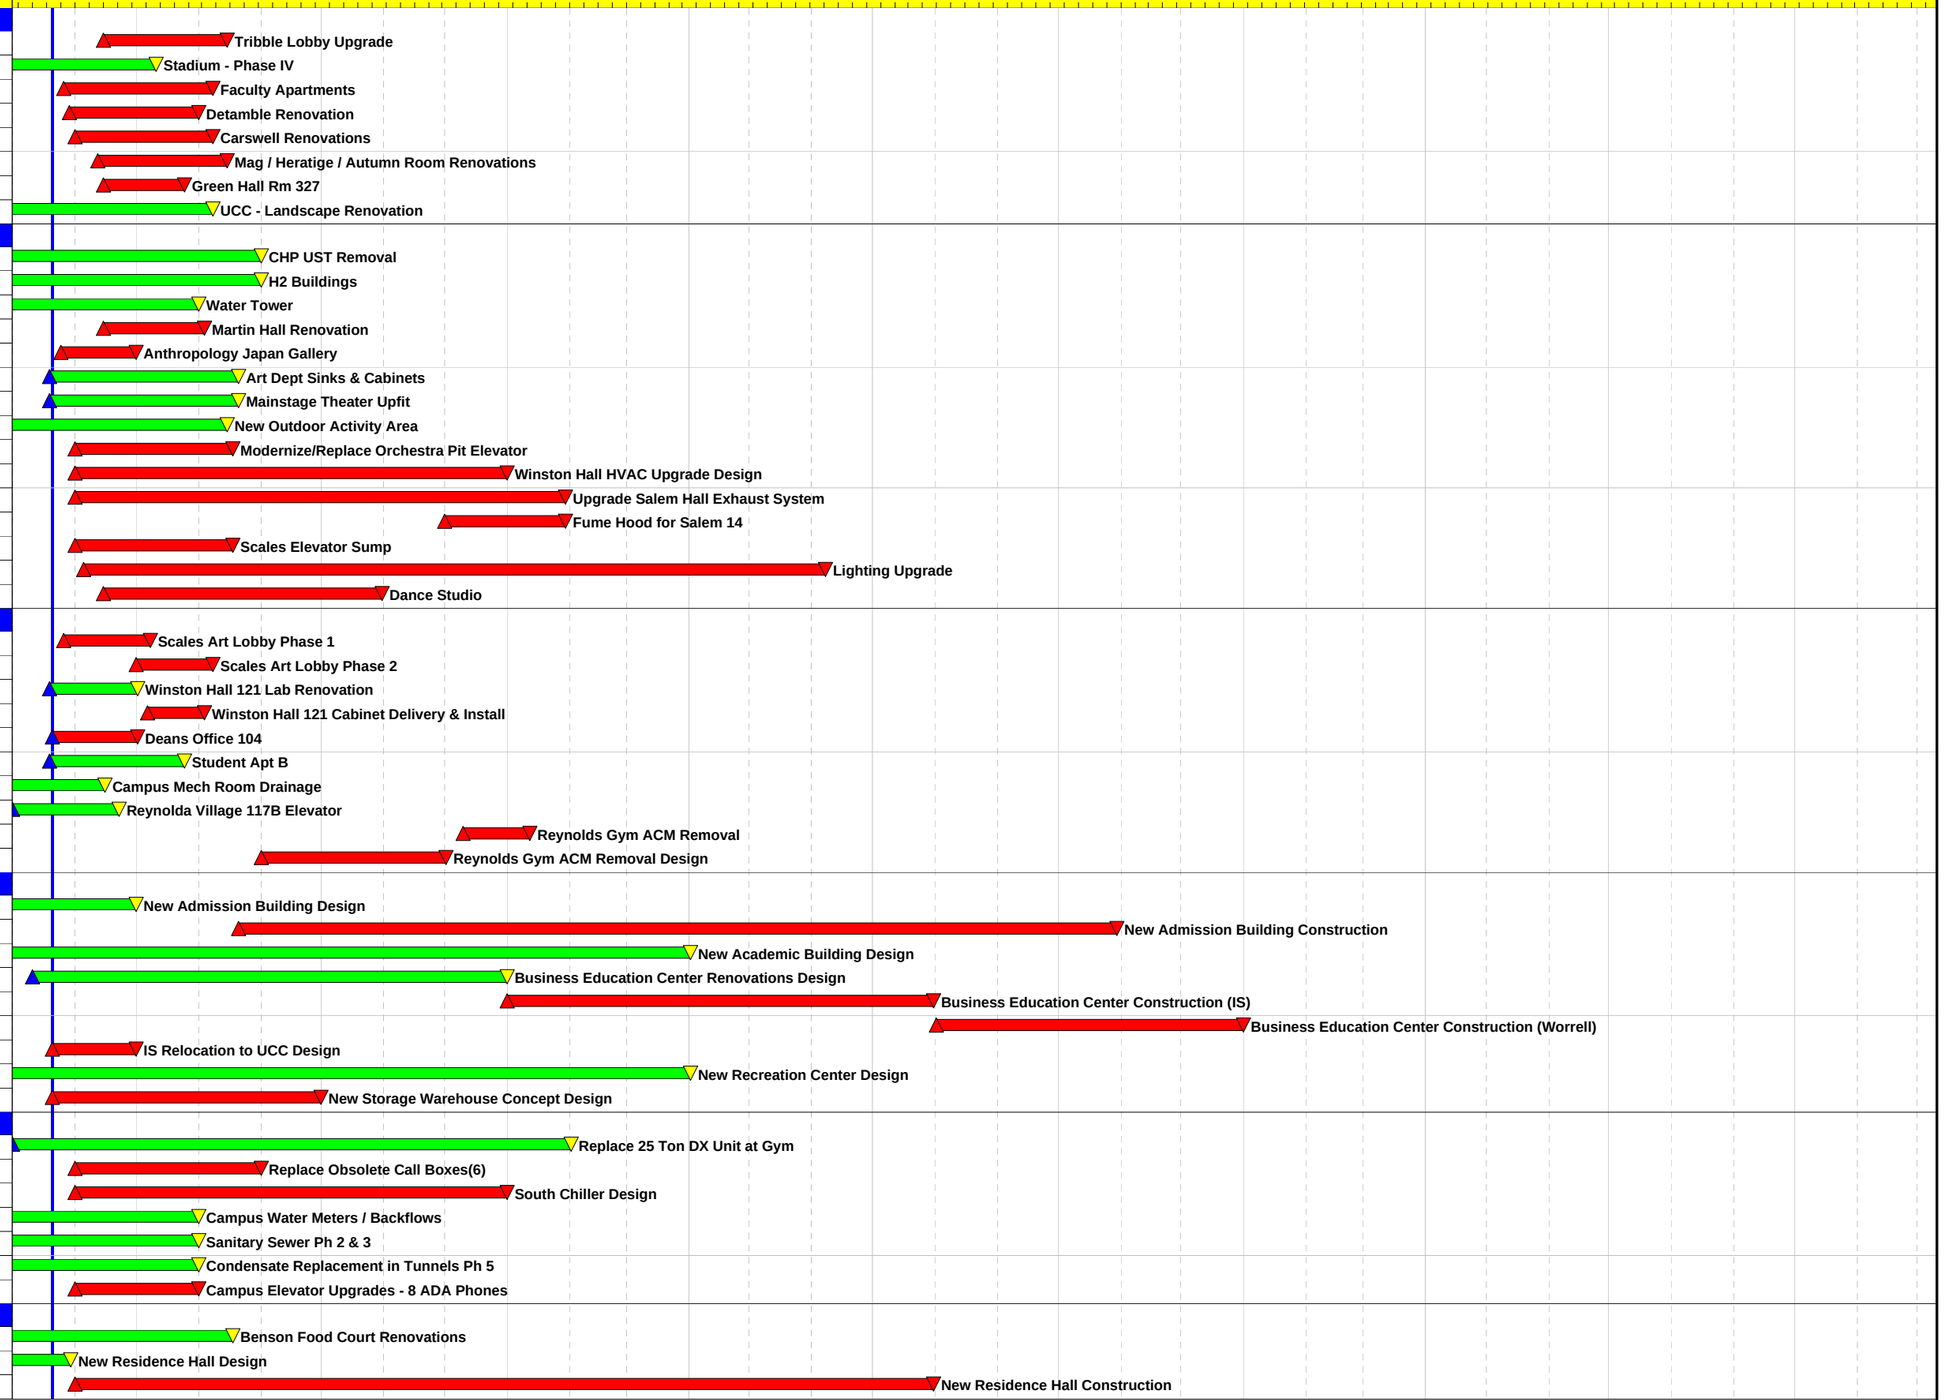


| | | |
|---|---|---|
| Project Start | 01AUG08 | Early Bar |
| Project Finish | | Progress Bar |
| Data Date | 21MAY09 | Critical Activity |
| Run Date | 28MAY09 | |

© Primavera Systems, Inc.

PMP1

WFU

Project Management Projects

Classic Schedule Layout
